Ignite | R2.1-A | SIT Test Plan

TPG Detailed Test Plan

Document Name	Ignite R2.1A SIT Test Plan
Version Number	0.1
Release Date	
Status	**In-Progress**
Document Author(s)	TCS

Contents

Version	Author	Date	Comments
V0.1	TCS		Initial Draft

Associated Documents and References

Document	Version	Location
Overall Solution Outline	NA	Ignite R2.1 – Technical Design Addendum - IT Architecture - Confluence
R2.1a & R2.0 Spill over - Requirements	NA	[Ignite_R2.1A & R2.0 Deferred items] Work item search - TPG Telecom Jira

iGnite(CMID) program overview		https://tpgtelecom.atlassian.net/wiki/spaces/CMID/overview?homepageId=9399265724670
Siebel Design Documents	V0.1	Siebel High Level Design R2.1a - Middleware, Inventory and Portability - Confluence
Pega Design Documents	v0.4 v0.1	R2.1 Container API Contract specification - Ignite (CMID) - Confluence R2.1 Pega Solution Outline and High Level Design: Data API (Capture Intent/NotPresentedReasons Process) - Ignite (CMID) - Confluence
Figma 2.1a		Ignite R2.1
UI/UX - Jira Ticktes		IPDGEN-19953: Ignite 2.1 RFD User Stories Detailed Design
Figma SFJ		VF strategic sales & fulfilment | v1
E2E Environments		Environments
Deferred Defects from R2.0		[Ignite_R2.1A_Deferred Defects] Work item search - TPG Telecom Jira

Distribution List

Name	Group/ Team	Role
Shannon Darcy	TPG Digital & IT	TPG Business Owner, Head of Marketing Technology and Decisioning
Nico Beauvillain De Montreuil	TPG Digital & IT	TPG Program Director
Jason Mercer	TPG IT BI	TPG Program Manager
Steven Davidson	TPG Digital & IT	TPG Project Manager
John Mathew	TPG Digital & IT	TPG Solution Architect
Chris Weskin	TPG Digital & IT	TPG General Manager ERP,BI Workforce

Pramod Pajjuri	TPG Digital & IT	TPG Program Test Manager
Manikandan PK	TPG Digital & IT	TPG Test Governance Manager
Prathibha Seetharaman	TPG Digital & IT	TPG BI Data Engineer
Nagarjuna Polimera	TPG Digital & IT	TPG AWS Data Platform Architect
Sankar Baskaran	TPG Digital & IT	TPG BSS Architect
Poppy Wilson	TPG Digital & IT	TPG Senior Product owner
Ipsita Saha	TPG Digital & IT	TPG Solution Architect
Nalin Liyanaarachchi	TPG Digital & IT	TPG Business Analyst
Arun Rangula	TPG Digital & IT	TPG Business Analyst
Meena Kesiraju	Accenture Digital & IT	Accenture Technology Delivery Lead
Parshant Sharma	Accenture Digital & IT	Accenture E2E Solution Architect
Abhitesh Kumar	Accenture Digital & IT	Accenture PEGA Lead
TJ Tupas	Accenture Digital & IT	Accenture Business Analyst
Lucas Monteiro	Accenture Digital & IT	Accenture Business Analyst
Pallavi Bhagavatula	Accenture Digital & IT	Accenture Tech Executive Lead
Siddharth Chaurasia	Accenture Digital & IT	Accenture Pega Lead system Architect
Archana Kumar	Accenture Digital & IT	Accenture Data Lead
Chanel Zhang	Accenture Digital & IT	Accenture Test and Release Lead
Alpana K Bange	Accenture Digital & IT	Accenture Test Lead
Tanushree Paul	Accenture Digital & IT	Accenture Data Test Lead

Abhishek Nikam	TCS BSS /IT	TCS Delivery Manager
Pritish Paniyadi	TCS BSS /IT	TCS IT Project Manager
Saravanan Jayachandran	TCS BSS /IT	TCS Siebel Architect
Saranya Nagarajan	TCS BSS /IT	TCS Test Lead
Karthickgoutham Raajah	TCS BSS /IT	TCS Test Lead
Vinod M	TCS NPE BSS /IT	NPE Lead
Rama Pydipati	TPG NPE BSS/IT	NPE Manager
Rohan Pai	TPG Digital/IT	TPG Project Manager - Imagine Project
Gauri Kashyap	TPG Digital/IT	TPG Test Governance Manager - Imagine Project
Ravi Kiran Boyapati	TCS BSS/IT	TCS Test Delivery Manager - Imagine Project

Review and Approvals

Name	Role	Approved Version	Approved Date
@Steven Davidson	TPG Project Manager		
@John Mathew	TPG Solution Architect		
@Manikandan Palaniyandi Kunchidhapatham	TPG Test Governance Manager		
@Meena Kesiraju	Accenture Technology Delivery Lead		
@Sankar Baskaran (Deactivated)	TPG Solution Architect		
@Ipsita Saha	Digital & IT - TPG Architect		

1. Introduction

1.1 Purpose

The purpose of this document is to detail the Test Plan for iGnite - Release 2.1 A

This plan will outline how the testing will be conducted, what will be tested, what will not be tested and who will be responsible for the various components of the testing.

1.2 Intended Audience

The intended audience for this document is:

- Project Managers
- Product Owners
- Architects
- Business Analysts
- Testing Consultants

1.3 Project Overview

- The aim of the Campaign Modernisation and Intelligent Decisioning (CMID) project is to transform TPG Telecom's Customer Lifecycle Management capability through:
- Deploying platforms and capabilities that leverage best-in-class Always-On Marketing and Next Best Action solutions powered by advanced analytics/machine learning models,
- Delivering personalised, relevant, and highly effective offers and experiences to our customers across any channel they interact with us,
- Optimising both customer experience and commercial outcomes through increased retention, cross-sell and upsell.

Below are some of the key objectives of this project:

- Ingestion of Real-Time data & Insights around customers and their interactions into the marketing platform.
- Using all available data points and triggers to make effective marketing decisions – automated, timely and at scale.
- Creating feedback loops into the decisioning engine to enable continuous optimisation driven by advanced analytics and machine learning.
- Building marketing platforms that are flexible and responsive to the constant market changes.
- Seamlessly integrate the decisioning and recommendations into all channels to improve customer experience and conversion.

- This ABTL (Automated Below The Line) initiative will allow the business to have a single source of truth for storing all products and rewards as well as a robust framework for automated fulfillment of these bundled or standalone through assisted and un-assisted channels. This program in conjunction with the centralised decisioning engine (Pega CDH) will improve customer experience, and will enable customers to receive real time strategic offers that will reduce churn and increase revenue. Building a framework to support offering bespoke offers to existing customers is a key driver for a successful retention program

Ignite R2.1A Solution Enhancements:

R2.1 addresses a set of design gaps, fulfilment inconsistencies, and new requirements raised after the R2 SAD was baselined. These items emerged through:

- R2 Open Items
- R2.1 Kanban board
- Siebel SSJ/F Interlock Alignment

Key objectives of Ignite R2.1-A include:

R2.1 enhances the R2 solution across Decisioning (Pega CDH), Siebel SSJ fulfilment, and downstream layers. The focus is on:

- Expanding ATL/BTL offer handling
- Standardising discount logic and FixedDiscount behaviour
- Improving some offer types handling (Content, Credit Governance)
- Improving missed-offer handling and bulk provisioning
- Strengthening fulfilment consistency across R1/R2 agents
- Enabling channel-specific behaviour (Single Price Per Plan)
- Enhancing dynamic Customer Intent
- ~~Extending Illuminate data coverage~~
- Improving auditability and reporting

R2.1a does **not** introduce new integration patterns.

Overall, R2.1a is an **incremental update to enable GTM** — designed to strengthen fulfilment consistency, improve visibility, and extend offer decisioning coverage, or major architectural shifts. R2.1a introduces **Container API V2** to support non-breaking schema changes related to Request payload (AgentDetails, CreditCheckDetails and Contexts) restructuring.

R2.1a will consume data from the Teradata → GDM → AL/CIC → Pega CDH,

TBC

Figure1 : Release 2.1A Solution Architecture Diagram

2. Solution Overview

2.1 In-Scope (Ignite R2.1A) :

New Requirements:

CLMNBA-3568 - Ability to Recommend Fixed Discounts Independent of Contract Duration

- This capability enables Pega to recommend ATL (Above The Line) and BTL (Below The Line) offers where the total discount amount is fixed (e.g., $400 off), regardless of the contract duration selected by the customer.
- The monthly repayment is calculated by dividing the discounted total price by the selected term, allowing for minor rounding differences.

CLMNBA-3852 - Enhance Container API to include Dealer and Channel Context Attributes

- Currently, only *RetailDealerCode* is included in the Container API request. To provide richer sales context, the API will be enhanced to include *SalesChannel* (e.g., Retail, Online, DMP) and *DealerGroup* (e.g., Smart Phones, TeleChoice).
- These attributes will be sourced from Siebel dealer metadata and will be used by Pega for data enrichment (IH/DH extracts) and future decisioning enhancements.
  There are **no changes to decisioning logic or response contract** for R2.1; this is purely contextual enablement.

CLMNBA-3630 - Credit recommendation

- In R1, agents issued one-off account credits (e.g., $30) via manual adjustments outside the cart flow; Pega only recommended them.
- In R2, fulfilment journeys live in Siebel/SSJ/TBUI and there is no direct cart journey for credits. Credits are also not cart-based, which limits the Pega feedback loop and learnings.

CLMNBA-3854 - Ensure consistent tracking of all Pega-recommended offers (Type 0–3) in Siebel for reporting and attribution

- Currently, **Type 0 (ATL) offers** provided by Pega CDH are **not captured in Siebel's CX_Offer_History** with their associated **Interaction ID**, leading to partial visibility of Pega's contribution in offer reporting.
- While Types 1–3 are already tracked correctly, the absence of consistent tagging for Type 0 creates reporting and attribution gaps across fulfillment and downstream analytics layers (MDS/Illuminate).

- Additionally, offers that are **not driven by Pega** — such as those **added manually in SSJ** — should be **explicitly excluded** from Pega attribution by ensuring they do **not carry a Pega_Interaction_ID** and their **offer_source ≠ 'Pega'**.
- To make the framework future-proof, this story standardises offer tagging across **all offer types** and ensures that any **Pega-originated recommendation** — irrespective of the offer channel or fulfillment type — carries the correct attribution metadata.

CLMNBA-3570 - Type 1 Offer inclusion in Decisioning & Offer Tiles

- This capability enables Pega to recognise and transmit Type 1 ATL inclusions (e.g., extra data, IDD minutes, ATL price adjustments) so they can be used in engagement policy and arbitration and clearly displayed on offer tiles (for example, in the “offers” section or equivalent channel widget).
- Pega applies transient overlay attributes before engagement policy and arbitration, ensuring conditional ATL (e.g., “new services only”) is evaluated correctly and presented consistently across channels.

CLMNBA-3650 - Offer Section for recommendations

- Recommendations may include additional inclusions beyond the standard plan benefits (e.g., “20GB Extra Data”, “100 Z1 Minutes”).
- These inclusions can be Above-the-Line (ATL) or Below-the-Line (BTL). Pega will supply these items concatenated in a single field named **WhyRelevant** at the **parent** action level, with each inclusion separated by a pipe (`|`).
- The UI must split and present these items on the **offer section tile**, in a dedicated area **outside** the standard Benefits list.

CLMNBA-3798 - Add on Inclusion in Recommendations (RPC/Upgrade & Standalone)

- The business requires flexibility to offer add-ons either bundled with a plan/contract change or independently, allowing customers to receive tailored benefits.
- Add-ons may be free rewards (no price) or discounted in-market add-ons (AU Code + Discount).
- The capability must handle all combinations—RPC, Upgrade, and Standalone—ensuring correct payload construction, fulfilment integration, and UI clarity.

CLMNBA-3649-Credit offer lifecycle

- Credits (discounts) with a duration longer than one month may remain active across plan changes and service events.

- We need clear, deterministic rules for when a credit is **kept** or **dropped** after each event, so agents and customers experience consistent outcomes and billing remains correct.

CLMNBA-3659 - Stackability and Co-existence

- We are standardizing how offers being recommended at the same time can sit together (stack) and whether a newly accepted offer should keep or replace an existing one on the same service (co-existence).
- Stackability is simplified to default behaviours, removing the need for an explicit flag. This aligns the experience across ATL/BTL.

CLMNBA-3664 - Order Compliance until fulfilment

- We must prevent invalid combinations (e.g., a plan-only discount that actually requires a device) while keeping the UI responsive.

CLMNBA-3893 - Uplifted UI (Ignite R2.1 Figma)

CLMNBA-4900 - Enforce “Applicable Quantity” for New Service Offers in Pick & Mix

- Certain offers must be capped so customers or agents cannot add unlimited quantities of the same offer into the cart.

MOCN (FWA) - TBC

NBN Template (Fixed) - TBC

Deferred Items

Jira Id	Summary
NA	Strategic Fullfillment requirement
CLMNBA-3268 (AC-1/ AC2.1)	Go to Sales Calculator - Button/Functionality
CLMNBA-2661 (AC 1)	
CLMNBA-3111	Order Type-Change of Technology
CLMNBA-3850	BUS - Bulk Provisioning tool
CLMNBA-3591	BUS - Content Offers
CLMNBA-3892	Pause-Resume Functionality

CLMNBA-3887	BUS - R2 Offer List Groups (This is covered as part of other BUS deployment)
CLMNBA-3894	Fulfilment Monitoring Requirements
CLMNBA-3866	Offer Lifecycle Management
CLMNBA-3867	BUS - Offer Lifecycle Management for Type 3 Offers
CLMNBA-3677	BUS - Missed Offers (Back office process)
CLMNBA-3833	BUS - Missed offers - Incorrect Device
CLMNBA-3834	BUS - Missed offers - Incorrect Plan
CLMNBA-3838	BUS - Missed offers - Incorrect Offer
CLMNBA-3848	BUS - Missed offers - Due to System errors

Deferred Defects

Deferred Defect Id's	Current Status
CLMNBA-3960	Deferred Defect - Delivered in R2.1A
CLMNBA-4115	Deferred Defect - Delivered in R2.1A
CLMNBA-4112	Deferred Defect - Delivered in R2.1A
CLMNBA-3947	Deferred Defect - Delivered in R2.1A
CLMNBA-4448	Deferred Defect - Delivered in R2.1A
CLMNBA-4039	Deferred Defect - Delivered in R2.1A
CLMNBA-3977	Deferred Defect - Change in Req
CLMNBA-3978	Deferred Defect - Change in Req

CLMNBA-4001	Deferred Defect - Change in Req
CLMNBA-4040	Deferred Defect - Change in Req
CLMNBA-4124	Deferred Defect - Change in Req
CLMNBA-4052	Deferred Defect - Change in Req
CLMNBA-4155	Deferred Defect - Change in Req
CLMNBA-5287	Deferred Defect - Change in Req
CLMNBA-5308	Deferred Defect - Change in Req
CLMNBA-5272	Deferred Defect Must Fix in R2.1A
CLMNBA-5419	Deferred Defect Must Fix in R2.1A
CLMNBA-5314	Deferred Defect Must Fix in R2.1A
CLMNBA-5347	Deferred Defect Must Fix in R2.1A
CLMNBA-5352	Deferred Defect Must Fix in R2.1A
CLMNBA-5388	Deferred Defect Must Fix in R2.1A
CLMNBA-5045	Deferred Defect Must Fix in R2.1A
CLMNBA-5306	Deferred Defect Must Fix in R2.1A
CLMNBA-5313	Deferred Defect Must Fix in R2.1A
CLMNBA-5344	Deferred Defect Must Fix in R2.1A
CLMNBA-5346	Deferred Defect Must Fix in R2.1A

2.2 Out of scope

- **Prepaid products and offers**: The initiative focus exclusively on postpaid consumer offerings, excluding prepaid products and related promotions.
- **Business Segments**: Scope is limited to postpaid consumer offerings (incl. SoHo with consumer offering); business customers are not included.
- **Digital & Self-Service Channels**: Ignite R2 is focused only on human-assisted channels (Contact Centre & Retail); digital touchpoints remain unchanged.
- **AI/ML Model Development**: Decisioning improvements leverage existing Pega CDH models and MDS integration; new AI/ML model creation is not covered.

- **Onboarding of ESP vendor**: This will be handled with a separate SAD.
- **Decommission of current marketing platform**.
- **Pega interaction history data in SAS MA and RTDM**: This information will not be made available.
- **NPS campaigns to ResponseTek**: These will not be set up in the new platform.
- **Alerts & Triggers decision diagrams in SAS RTDM**: These will not be migrated into the new marketing platform.
- **MMS outbound channel**: This will not be built.
- **Integration into digital personalization tool**: Not included in this SAD.
- **Other TPG Telecom brands**: TPG, iiNet, Internode, Lebara, AAPT & Felix are not included in this phase.
- BI SIT Testing is not part of TCS scope for Ignite R2.1 A
- **Reporting**:
  - Integration with Illuminate MDS and enrichment of Pega CIC with ~137 new attributes.
  - Bring postpaid products and offer catalogue data from Siebel into Pega BoE environment for monitoring via MDS-Pega CIC data layer.
  - Build canned fulfilment reports (CLM, Finance, Cops, CoE)
  - Outgoing Data Enhancements:
    - Interaction History
    - Decision History
    - Action Catalogue Data (from Pega).

2.3 Test Process Overview

Test Planning

All test cases will be created from the functional/business requirements and business processes. Below are the list of items created during this phase.

1. Test Objective Matrix/Test scenarios
2. Test Cases
3. Test Results
4. Test Summary Report
5. Requirements Traceability Matrix (RTM)

Test Scenarios Walkthrough Sessions

Test scenario walkthrough sessions will be held with to understand what will be executed and get feedback on test coverage. All test scenarios/cases will have traceability back to the requirements (RTM).

Test Case Execution

During test execution the tester will go through what cases that will be executed for that day. All Test execution is tracked in JIRA.

Defects will be raised in JIRA by the tester. Defect Severity and Priority will be triaged during the test execution window or Defect triage meeting.

The Test Lead will publish a Daily Status Reports (DSR) to keep track of defects and issues raised and testing progress.

Test Summary Report

Once all testing is complete the Test Lead will write and publish a Test Summary Report (TSR). The TSR will provide an update on all test cases, what passed, failed, or made Not Applicable – and why. The TSR will show all defects raised and their end status. Approvers of this document will be asked to also approve the TSR – this document. This Test Plan outlines what and how things need to happen during the test phase, the TSR will outline what did happen during the test phase.

2.4 Test Approach

Test Phases	Test Objective	Environment	Responsible Team	Deliverables
Shakedown Testing	To verify that a deployment of the developed component (software, hardware/infrastructure) into a controlled test environment has been successful and the connectivity between the	SIT Env	TCS SIT Testing Team	Test cases

	applications is configured.			
System Integration Testing	System Integration Testing will focus on detailed testing to ensure all the E2E functionalities are verified across the planned/agreed platforms/applications	SIT Env	TCS SIT Testing Team	Test Plan Test Scenarios/TOM Test cases Test Results DSR TSR
User Acceptance Testing	Objective of the user acceptance test is to make sure the solutions meet the business requirement.	UAT, Prod	TCS SIT Testing Team (support) TPG Business Team (CLM/COPS)	TOM/Test Scenarios Test cases Test Results DSR TSR
Clean Run Regression Testing	Final Regression after code freeze	SIT/CRR	TCS SIT Testing Team	TOM/Test Scenarios Test cases Test Results DSR TSR
Cut over Verification Testing	Verify successful change implementation in PROD.	PROD	TCS SIT Testing Team	Test cases Test Results

Production Verification Testing	Verify successful change implementation after cutover in PROD.	PROD	TCS SIT Testing Team	Test cases Test Results

Note: OSS Testing, OAT Testing and Performance Testing are out of scope for this document [Separate DTP will be shared for Performance testing]

2.4.1 Test Data Approach

Data Setup for R2.1A SIT to get Offer Recommendations in Siebel

Phase 1: Data Conditioning at PEGA

1. Base Data Preparation

- Prepare **~200 records** of base data in **E2E12**.
- Include **different plan types** to ensure coverage across scenarios.

2. Base Data Batch Preparation

- Map the prepared base data to the **15 key CIC attributes**.
- Create a **Batch Sheet** containing this mapped data.
- Share the batch sheet with the **Pega Team** for conditioning.

3. Data Conditioning

- The **Pega Team** will perform the data conditioning **directly in PEGA CDH**.

Phase 2: Data Conditioning at TeraData

1. Base Data Preparation

- Prepare **~300 records** of base data in **E2EXX**.
- Include **different plan types** similar to Phase 1.

2. Base Data Batch Preparation

- Map the prepared data to the **same 15 key CIC attributes**.
- Create a **Batch Sheet** for TeraData processing.
- Share the sheet with the **BI Team** for conditioning.

3. Data Conditioning & Job Execution

- The **BI Team** performs data conditioning within **TeraData**.
- After conditioning, the BI Team will **trigger the job**.

4. Data Flow

Once the job is triggered, the data flows in the following order:

TeraData → GDM → AL/CIC → Pega CDH

2.5 RACI Matrix

Please note that the below matrix is just presented as an example, each project will need to adapt to its own matrix based on the responsibilities agreed.

Responsible Deliverables	TCS Test Team	TPG Architect	TPG Test Governance Manager	TCS Test Manager	Accenture Testing Team
SIT Test Plan creation	R	C	C	R/A	I
SIT Test Plan Approvals	R	C	C	R/A	R
SIT Test case Creation	R	C	C	R/A	I
Upload in JIRA	R	I	C/I	R/A	I
SIT Test Execution	R	C/I	C/I	R/A	C/I
SIT Test Results	R	C/I	C/R	R/A	R
Daily Status report	R	I	I	R/A	I
Test Summary report	R	C	C/R	R	R
TSR Approvals	R	C	C/R	R	R

Legend:

R-Responsible

A-Accountable

C-Consulted

I-Informed

2.6 Test Case Specifications

The test cases have been identified using the detailed requirements. All iGnite Program requirements can be found in the following location:

Link to project requirements: High Level Business requirements - iGNITE - Release 2

Below is the link for the cases saved in the common repository that will be executed as part of the test phase

Link to JIRA Project:CMID


2.7 Testing Schedule and Deliverables

The below is an illustration of the millstones for Test Phase, flowed by a schedule of deliverables produced by the Test team during the test phase:

Deliverable	Start Date	End Date	Responsible
Test Plan			TCS Testing Team
Test Plan Review			TCS Testing Team
Test Plan Approved			TPG & Accenture Stakeholders
TOM Preparation			TCS Testing Team
TOM Walkthrough			TCS Testing Team
TOM Approval			TPG & Accenture Stakeholders
Test Environment Readiness			Environment Team (TCS NPE) Accenture Team (Ignite & Illuminate)
Deployment to Test Environment			Accenture Team & TCS Dev/NPE

Test Data Preparation			TCS Testing Team Illuminate Team
Sanity Check / Shakedown Testing			TCS Testing Team
SIT Test Execution			TCS Testing Team
Test Summary Report			TCS Testing Team
Test Summary Report Review			TCS Testing Team
Test Summary Report Approved			TPG & Accenture Stakeholders

2.9.1 Test Execution Plan

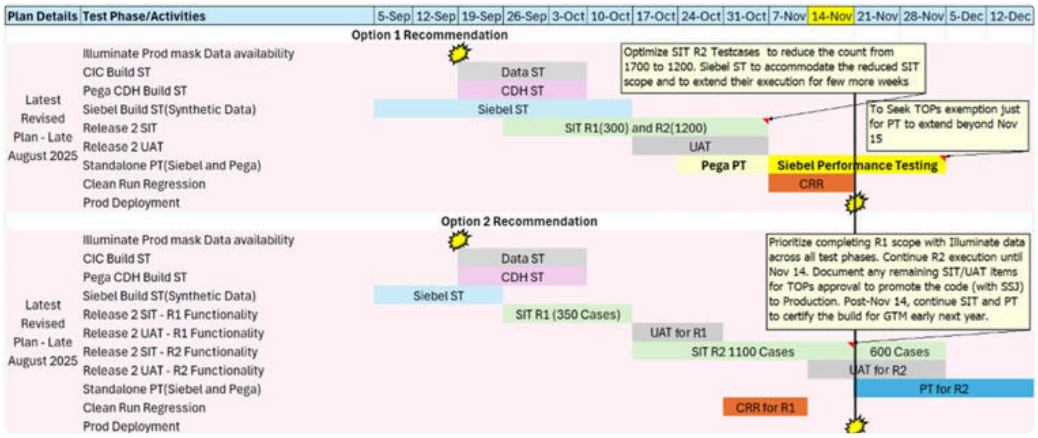

2.10 Test Tools

All test cases and defects will be documented in the JIRA. When a tester finds a defect, this will be triaged by Test Lead.

Tool	Purpose	Comments
Jira	Defect Management	Defects will be created and managed on Jira dashboard
Zephyr scale	Test Case Management	Test cases will be created and loaded into Zephyr scale and available for Test Execution

Putty	Test Execution	To execute the scripts for various scenarios.
WinSCP	Test Execution	File transfer process
SQL developer	DB Validation	To verify the results in DB.

2.11 Test Environment

Testing will be performed in (environment name) test environment. The URL is below:

Test Phase	Environment	Environment Type	Comments
ST Testing	Dev Environment	Stand Alone	Dev environment for PEGA Dev environment for Siebel, Fusion, GG and other key peripheral systems planned for integration Ignite R2
SIT Testing	SIT Environment	**Non-Prod Environment - Siebel E2E12**	Illuminate MDS <> PEGA CIC layer (TBC) <> MFT <> PEGA CDH DT2 <> Apigee<> Siebel <> Fusion <> BRM This integrated env will be used for Siebel integrated release SIT testing end to end. Also, this env will be an env that will cater to Imagine SSJ project testing
CRR Testing	CRR Environment	**Pre Prod Environment - E2E07**	Pre Prod Environment

CVT/PVT Testing	Production Environment	Prod Environment	Prod deployment

3. Entry/Exit Criteria

Entry criteria into SIT testing
Integrated environment to be setup & ready with required Infra, Platform Application DB & OS Upgrades
Access to the required environment & Tools
Required Test data and tools available.
System test completed 100% and exit criteria has been met for each impacted system as defined in Test Strategy with no open defects for each impacted system.
Any comms implementation for end-to-end connectivity between the applications must be setup, ready and working before commencing testing.
Shakedown testing completed successfully.
SIT Test Objectives Matrix (TOM) is approved.
SIT test cases has been prepared, reviewed, and loaded into JIRA after signed off.
Exit out of SIT criteria
All planned Tests are executed and passed
No outstanding Critical defects
No outstanding High priority defects, unless accepted by Project team
Test results /TSR shared and reviewed
Approved by Test Manager/Architect/Business Analyst/Project Manager

Entry criteria into CRR testing
SIT/UAT/Performance/CA Test completed and exit criteria has been met.
CRR test cases have been prepared, reviewed, and approved by core project delivery team.
Test Cases uploaded in JIRA and ready for test execution.

CRR environment is available and has been shakedown and is ready for test execution. Latest Code plus CRR package is deployed in CRR environment. As of date production pricing config baseline would be made available for CRR. Test data is available for test execution.
Exit out of CRR criteria
All planned CRR test cases must be executed and passed successfull. All test results and defects have been recorded. No outstanding severity 1 or severity 2 defects. All outstanding severity 3 and severity 4 defects have a resolution plan in place and is accepted by the core project delivery team CRR Test Summary Report have been produced and approved

Entry criteria into CVT testing
CRR Test completed and exit criteria has been met. CVT test approach and test cases have been created and approved by core project delivery team including key business stakeholders. Support resources and procedures are in place for testing
Exit out of CVT criteria
All business critical and mandatory test cases have been completed successfully. No outstanding severity 1 or severity 2 defects All outstanding severity 3 and severity 4 defects have a resolution plan and/or work around in place and is accepted by the core project delivery team and key business stakeholders. A “Go” or “No Go” decision has been made

Entry criteria into PVT testing
A “GO” decision has been made and exit criteria has been met. PVT test approach and test cases have been created and approved by core project delivery team including key business stakeholders.

Support resources and procedures are in place for testing
Exit out of PVT criteria
All business critical and mandatory test cases have been completed successfully.

3.1 Defect Classification

Severity

Severity is an objective measure of the impact that the defect has on the product. This should be based on what the impact would be if the defect were to occur in production. The severity will be assigned based on the following criteria:

Severity	Criteria
Severity 1 – Critical	A critical issue is where a large piece of functionality or major system component is completely broken. There is no workaround.
Severity 2 – Major	A major issue is where a large piece of functionality or major system component is not working properly but a workaround exists, or a moderately used piece of functionality is completely broken.
Severity 3 – Moderate	A moderate defect prevents full use of features but can be avoided using workarounds.
Severity 4 – Minor	A minor issue that imposes some loss of functionality, but for which there is an acceptable workaround.

Priority

Priority is a subjective measure on how important it is that the defect is fixed. The testing team will set the initial priority which may be changed following discussion at the defect management meeting.

The priority will be assigned based on the following guidelines:

Priority	Guidelines
Blocker (Priority 1)	The issue completely blocks testing progress. The product cannot be used by the business or deployed to production. No functional area can be tested.
Critical (Priority 2)	This has a critical impact on test progress. The product cannot be used by the business or deployed to production. Major functional areas cannot be tested.
Moderate (Priority 3)	This has a moderate impact on testing. The flaw should be fixed if there is time, but it can be deferred until the next release.
Minor (Priority 4)	There is no concern about when this defect is resolved as it does not impact test progress.
Trivial (Priority 5)	The defect is trivial in nature and is related to issues like incorrect font, size, color.

Priority/ Severity Type	Definition	Response Time	Targeted Resolution Time
P1	Critical - cannot progress further (showstopper). Must be resolved ASAP. Examples: Essential function is not working at all, and no practical workaround exists. Program aborts or stops. Serious database corruption.	< 1 hour	< 24 hours

	Major interface problem which stops down-stream processes		
P2	High - serious impact, possible work around. Must be resolved ASAP. Examples: Essential functions are severely restricted. Essential function not working, practical workaround available. Restricted performance, logic problem. Causes severe restriction to essential up-stream or down-stream processes.	< 12 hours	< 48 hours
P3	Medium - low impact, workaround available. Does not need to be resolved before go-live but workarounds must be formally documented. Examples: Records out of sequence. Misleading message. Misleading user guides	< 24 hours	Based on time and effort estimation
P4	Low - not serious, cosmetic. Does not need to be resolved before go-live but workarounds must be formally documented. Examples: Incorrect color or font	48-72 hours	Based on time and effort

4 Risks, Assumptions, Issues, and dependencies

4.1 Risks

Sno	RiskID	Phase	Risk	Impact	Likelihood	Suggested Mitigation Plan
1	#R001	Shakedown	Any delay in support required from Dev teams/other application teams (TD, GDM, CMID, PEGA) team during shakedown phase will delay SIT execution.	High	High	Alignment with application teams for required support during shakedown test period
2	#R002	SIT	SIT Environment should be ready and available for the testing	High	Medium	Track env readiness for the test phase closely and call out any deviation to the planned dates.
3	#R003	SIT	Comms to be established for all the required systems/applications for SIT testing. Failing to meet this will impact the SIT testing	High	Medium	Clear communication on the comms /integration implementation and checks conducted

						by respective team to avoid comms failure .
4	#R004	General	Schedule impact due to high number of defects / poor code quality (if this risk eventuates then it will become an issue)	High	High	Testing team to ensure that exit criteria is met and have the Test cases and Results reviewed and approved by Test Manager and Solution Architect
5	#R005	General	Any delay in defect turn around time from vendors team or Dev support , environments will have an impact in planned testing schedule	High	High	Daily meetings with vendor support teams.
6	#R006	General	Change in scope after any	High	Medium	Change in scope after testing

			testing has started			starts will potentially result in testing and project timelines to be revised
7	#R007	General	Change in test environment where a test phase is planned for execution after scope finalization will potentially impact testing timelines as execution impact may defer between environments	Medium	Medium	Ensure environment is agreed and locked down before test execution commences.
8	#R008	Test Data	Data should be created and ingested to PEGA CDH via Illuminate MDS. Any deviation in this approach will be treated has very high risk for Ignite R2 SIT	High	High	Test data creation and shakedown with ingested data must be completed before SIT kick start

9	#R009	Synthetic Test data for SIT	**Inadequate E2E Testing and Production Impact** • Using synthetic data for our end-to-end (E2E) testing may not fully replicate real-world scenarios. This creates a significant risk that defects, particularly those related to data integrity and user behavior, will not be identified before we go live. This could lead to critical production issues for R1 in Nov. **PEGA Decisioning and System Integrity** • The effectiveness	High	High	Get actual production masked data to be ingested from illuminate to PEGA

			of the PEGA decisioning engine is highly dependent on a realistic and diverse data set. Synthetic data may not contain the necessary complexity or edge cases to properly validate the decisioning logic, increasing the chance of incorrect system behavior once deployed. **Testing Delays and Unforeseen Defects** • The use of synthetic data is likely to result in a higher number of unforeseen defects during the System Integration			

			Testing (SIT) phase. The effort required to investigate and resolve these issues could cause a significant extension of our SIT timeline, potentially impacting our release schedule. **Lack of Reference for the New R2 Component** • The new R2 component has no existing reference points for data validation. Without a realistic data set, we lack the ability to ensure the new component is integrated correctly and functions as			

			intended. This makes it challenging to provide 100% confidence in the quality of the data setup.			

4.2 Assumptions

Description of Assumption
1. Project scope will not change once the TOM & Test cases are approved. Any changes to scope will be mutually governed and discussed.
2. A stable environment will be available to the project teams during test execution phase. No significant change to the environment will occur once test stage is commenced.
3. Base Data preparation owned by SIT Testing Team (TCS) and Data Ingestion to PEGA CDH for specific data available in E2E environment for different type of scenarios owned by Illuminate team & PEGA Team (Accenture)
4. Any change requirements will need to go through an impact assessment from timeline, effort, and scope perspective.
5. Not all offers/rules/scenarios will be tested and only required functionality will be tested and the same has to be approved by architect
6. Raised defects are fixed on time as per defect SLA.
7. Approvals for the Test Strategy, TOM, Test Summary Results, and all other applicable test artefacts will be received on time.
8. Offer Recommendation validations will be mix and match for different scenarios for different customer type and offers. 1:1 offer mapping test is not considered. The no.of test cases will increase if we need to test each offer & change applicable w.r.t each offer, and additional time is required if it has to be catered.
9. Shutdown period support is considered - TBC as we will require other team support as well to perform effective test execution.

10. Since UAT scope is not yet defined, only minimal test data support effort is considered. If further support is required, it will be a CR.
11. 5% of progression scenarios only considered to validate invoices for different offers. No regression testing is considered
12. it is not feasible to fulfill an SSJ Quote and a PEGA (R1 or R2) recommendation within a single order journey. Agents must complete these in separate order journeys.
13. Ignite will use SSJ capabilities to get plans, devices, and prices directly from the Siebel BAU Matrix.

4.3 Dependencies

Description of Dependency
1.Complete code deployed in the test environment
2.All the test logins setup correctly
3.Environment up and running prior to start of test execution
4.All ST & env defects will be resolved on the agreed SLA's
5.System Testing completed for all components with No Severity 1 & 2 defects
~~6.Business config team to setup the promo codes in Siebel for Testing~~
7. Offer catalogue/Matrix to be provided for Test Planning activities
8. Siebel/Pega UIUX screens to be provided for Test Planning activities
9. Sharing SIT environment with Imagine project and expecting environment stability throughout project
10. Illuminate team & Pega team support required throughout the project schedule for offer configuration for specific data available in E2E environment, SIT support, Production testing support
11. Illuminate is tasked with ingesting production masked data from Illuminate MDS to PEGA CDH by ~~September 15th~~ October 15th-. We'll perform a week of sanity testing, and the official Tranche 2 SIT will begin on ~~September 22nd~~ October 20th.

13. New Ignite R2 reward offer products configured from Pricing Config Team for Fulfilling new offers introduce in R2

4.4 Issues

Description of Issue	Mitigation	Created Date

5 Approvals

Name	Email attachment

6 Appendix

Deferred Requirements (R2 to R2.1) - Ignite R2.1 WIP - Kanban Board - TPG Telecom Jira
